




San Rafael City Schools Measures A and B Bond Facilities Program Schedule June 2019 Update



Activity Name	Duration	Start	Finish	2016												2017												2018												2019												2020												2021																													
				M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A																
San Rafael City Schools Measures A and B Bond Facilities Program																																																																																													
Measure A Bond Facilities Program																																																																																													
10 Wing Roofing and Waterproofing																																																																																													
10 Wing Roofing and Waterproofing	730	01-Jun-16 A	01-Jun-18 A	[Bar]												[Bar]												[Bar]																																																																	
Davidson Middle School																																																																																													
New STEAM Classroom Building																																																																																													
District Programming	105	02-Dec-16 A	17-Mar-17 A	[Bar]												[Bar]																																																																													
Schematic Design	79	01-Apr-17 A	19-Jun-17 A	[Bar]												[Bar]																																																																													
Design Development	114	01-Jul-17 A	23-Oct-17 A	[Bar]												[Bar]																																																																													
Construction Documents	148	01-Feb-18 A	29-Jun-18 A	[Bar]												[Bar]																																																																													
DSA Approval	0		24-Jun-18 A	[Bar]												[Bar]																																																																													
Board Approval	0		27-Aug-18 A	[Bar]												[Bar]																																																																													
NTP	0	04-Sep-18 A		[Bar]												[Bar]																																																																													
Construction	406	10-Sep-18 A	30-Nov-19	[Bar]												[Bar]																																																																													
LLB/Bid Period	71	25-Jun-19*	03-Sep-19	[Bar]												[Bar]																																																																													
Move -In	56	21-Oct-19*	15-Dec-19	[Bar]												[Bar]																																																																													
Closeout	76	16-Oct-19*	30-Dec-19	[Bar]												[Bar]																																																																													
Bahia Vista School																																																																																													
Shade Structure	140	24-Jul-17 A	11-Dec-17 A	[Bar]												[Bar]																																																																													
Venetia Valley K-8 School																																																																																													
Transitional Housing																																																																																													
Design	98	22-Jan-18 A	30-Apr-18 A	[Bar]												[Bar]																																																																													
DSA Approval	1	01-May-18 A	01-May-18 A	[Bar]												[Bar]																																																																													
NTP	0	19-Jun-18 A		[Bar]												[Bar]																																																																													
Construction	72	19-Jun-18 A	30-Aug-18 A	[Bar]												[Bar]																																																																													
2 Story Classroom Building and MPR																																																																																													
Programming	90	01-Oct-16 A	30-Dec-16 A	[Bar]												[Bar]																																																																													
Design	161	08-Jan-17 A	18-Jun-17 A	[Bar]												[Bar]																																																																													
DSA Approval	98	10-Apr-18 A	17-Jul-18 A	[Bar]												[Bar]																																																																													
NTP	0	20-Sep-18 A		[Bar]												[Bar]																																																																													
Construction	773	21-Sep-18 A	01-Nov-20	[Bar]												[Bar]																																																																													
Move -In	50	01-Nov-20	20-Dec-20	[Bar]												[Bar]																																																																													
Closeout	13	21-Dec-20	02-Jan-21	[Bar]												[Bar]																																																																													
Glenwood																																																																																													
District Programming	12	01-Jun-18 A	13-Jun-18 A	[Bar]												[Bar]																																																																													
Schematic Design	27	06-Mar-17 A	02-Apr-17 A	[Bar]												[Bar]																																																																													
Design Development	139	03-Apr-17 A	20-Aug-17 A	[Bar]												[Bar]																																																																													
Construction Documents	79	21-Aug-17 A	05-Nov-17 A	[Bar]												[Bar]																																																																													
DSA Approval	0		06-Mar-18 A	[Bar]												[Bar]																																																																													
LLB/Bid Period	14	02-Apr-18 A	16-Apr-18 A	[Bar]												[Bar]																																																																													
Board Approval	0		14-May-18 A	[Bar]												[Bar]																																																																													
NTP	0	22-May-18 A		[Bar]												[Bar]																																																																													
Construction	341	14-Jun-18 A	20-May-19 A	[Bar]												[Bar]																																																																													
Move -In	30	22-May-19 A	20-Jun-19	[Bar]												[Bar]																																																																													
Closeout	51	01-May-19 A	20-Jun-19	[Bar]												[Bar]																																																																													

DRAFT

DRAFT

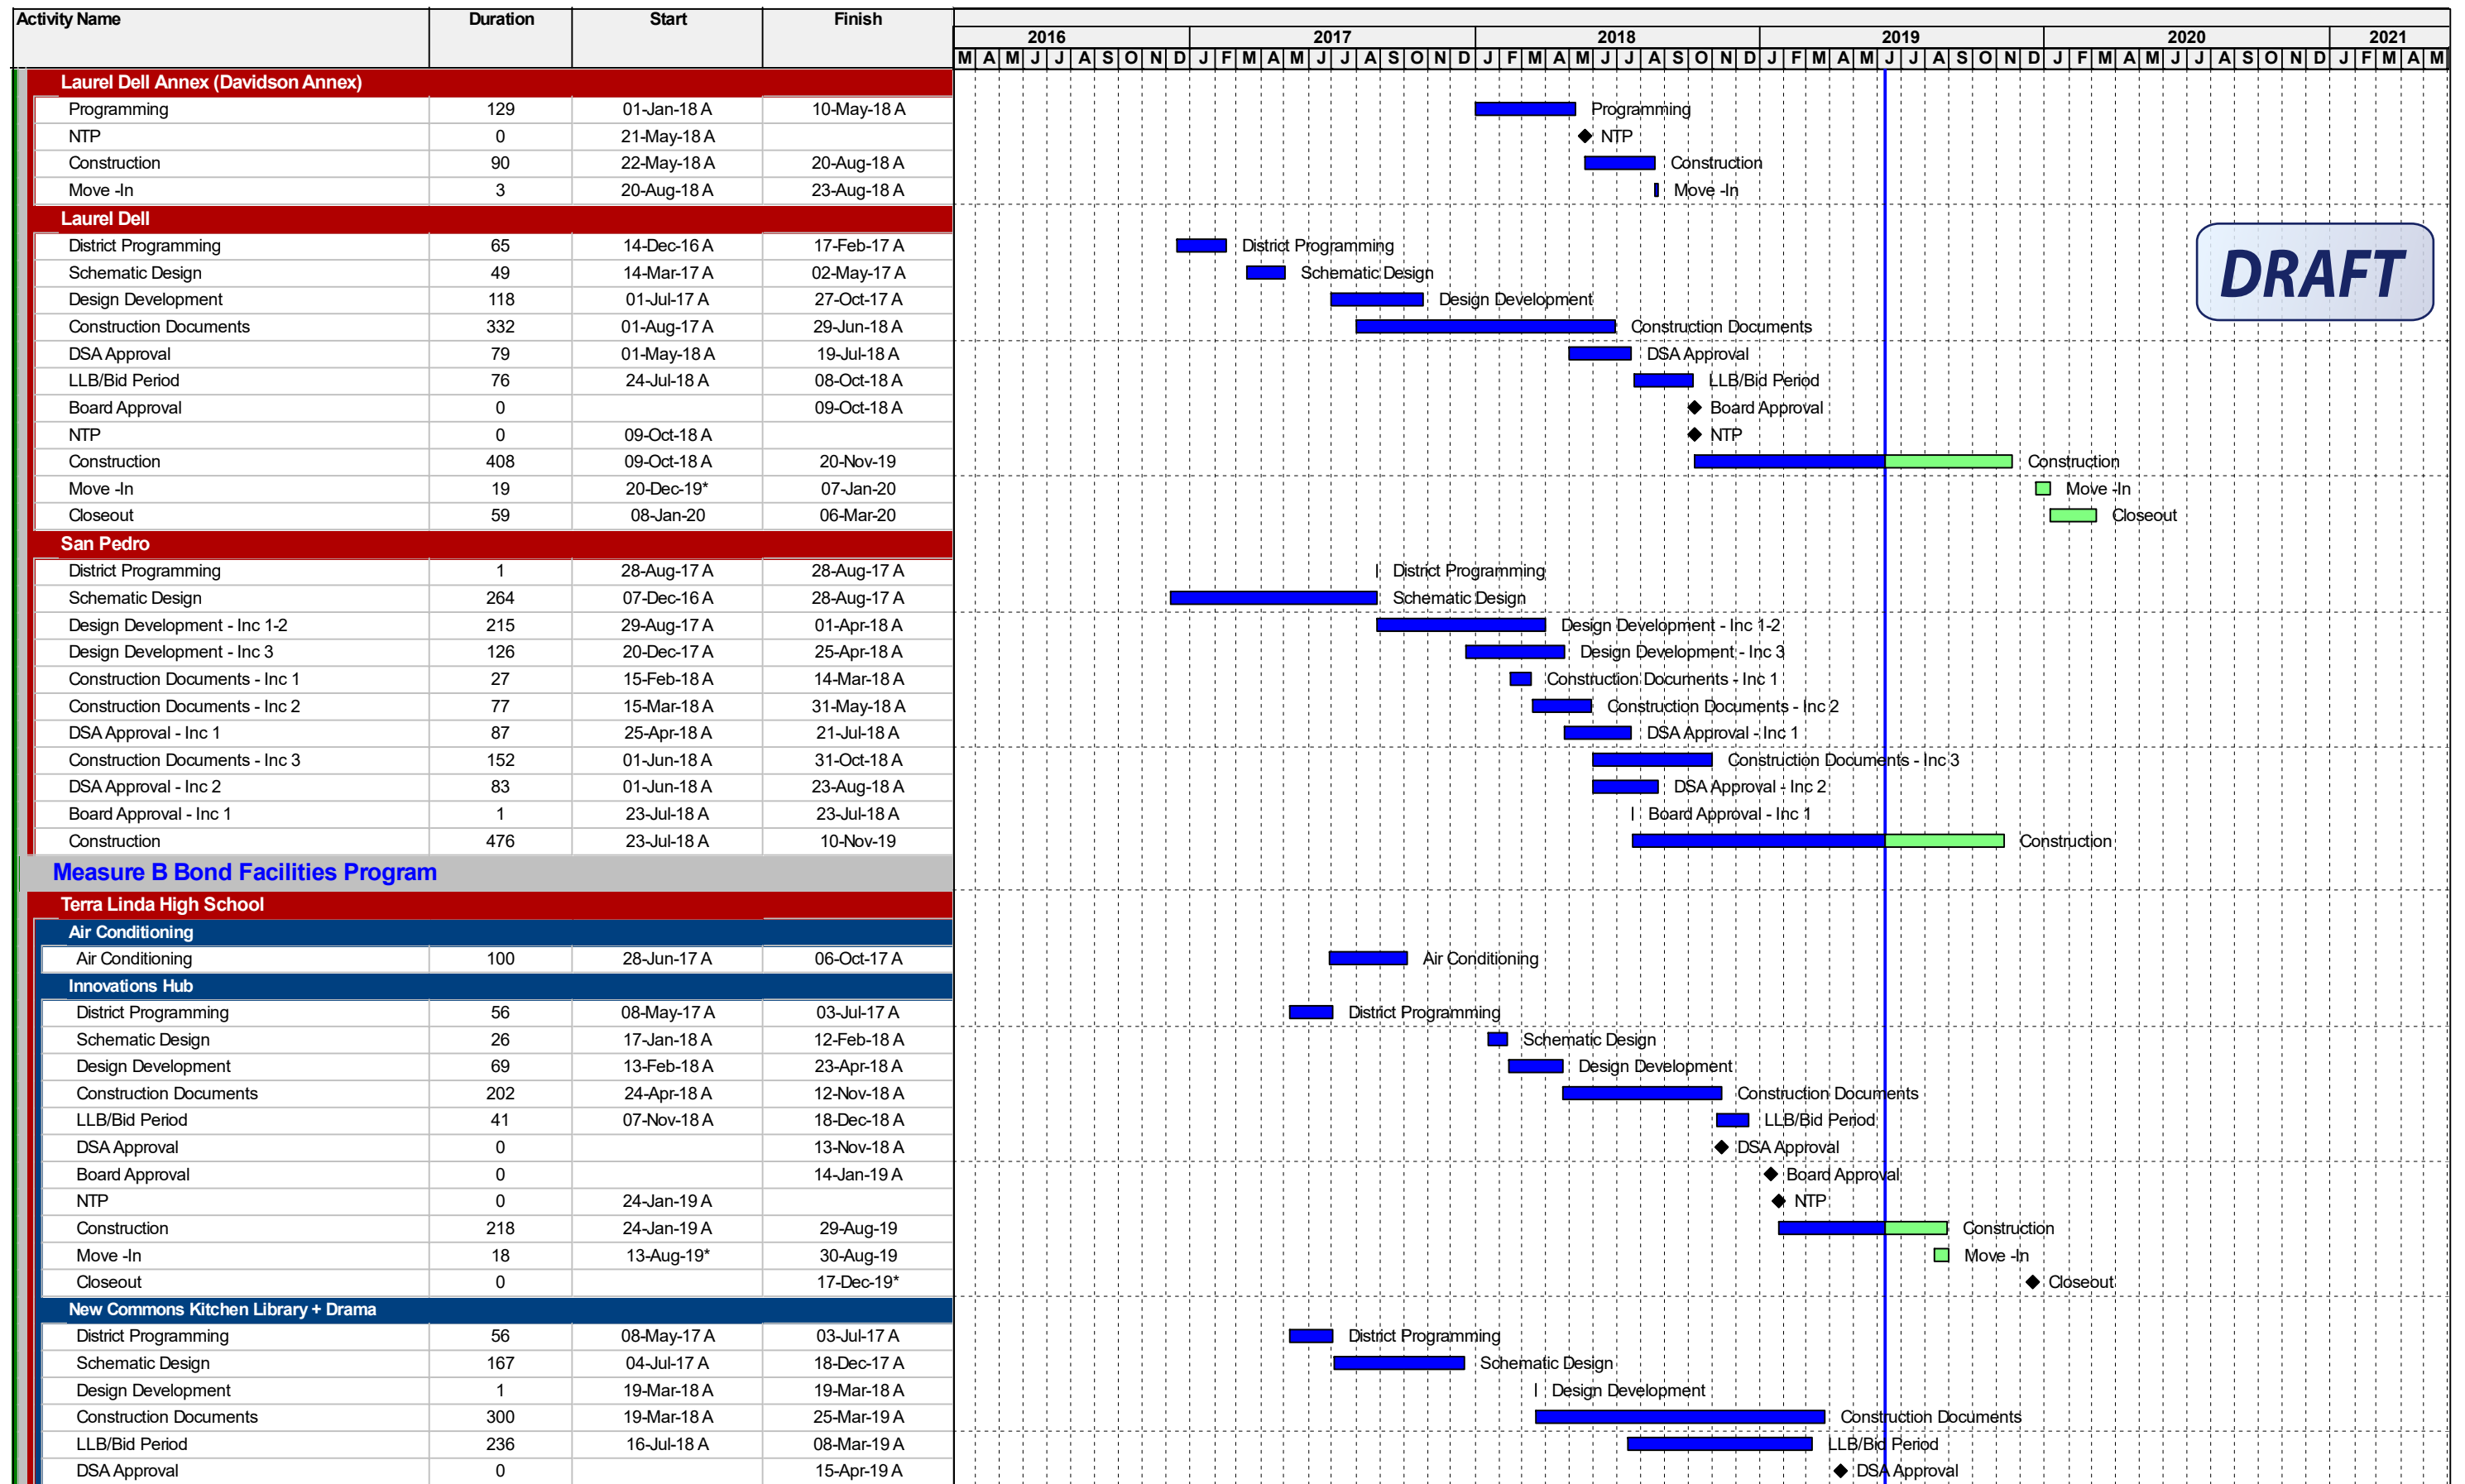

Activity Name	Duration	Start	Finish	2016												2017												2018												2019												2020												2021							
				M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M					
Board Approval	0		15-Apr-19 A																																																																				
NTP	0	01-May-19 A																																																																					
Construction	624	01-May-19 A	13-Jan-21																																																																				
Move -In	18	14-Jan-21*	31-Jan-21																																																																				
Closeout	23	14-Jan-21*	05-Feb-21																																																																				
New Music Building (FUTURE)																																																																							
New Main Gym (FUTURE)																																																																							
San Rafael High School																																																																							
Stadium Renovation																																																																							
Stadium Renovation	500	26-Jun-17 A	08-Nov-18 A																																																																				
Air Conditioning																																																																							
Air Conditioning	100	28-Jun-17 A	06-Oct-17 A																																																																				
Transitional Housing																																																																							
LLB/Bid Period	35	12-Apr-18 A	17-May-18 A																																																																				
Board Approval	0		29-May-18 A																																																																				
NTP	0	15-Jun-18 A																																																																					
Construction	51	25-Jun-18 A	15-Aug-18 A																																																																				
Move -In	4	06-Aug-18 A	10-Aug-18 A																																																																				
Closeout	125	10-Aug-18 A	13-Dec-18 A																																																																				
Commons, Kitchen, Admin, and Madrone (FUTURE)																																																																							
District Programming	1	03-Feb-17 A	26-Jun-17 A																																																																				
Schematic Design	1	24-Jul-17 A	18-Dec-17 A																																																																				
Design Development	990	19-Dec-17 A	02-Mar-18 A																																																																				
Madrone, Admin, Commons, Kitchen "MACK"																																																																							
Bid	0	30-Jan-19 A																																																																					
Construction	655	12-Mar-19 A	25-Dec-20																																																																				
Move-In	30	20-Dec-20*	18-Jan-21																																																																				
Closeout	74	19-Jan-21	02-Apr-21																																																																				
New CTE Science Engineering Tech. (FUTURE)																																																																							
Parking, Quads, + Site Work (FUTURE)																																																																							
Convert Old Admin to CR's (FUTURE)																																																																							

DRAFT
