


November 16, 2018

Venetia Valley School Supplemental Construction Update

Storm Drain Installation at Bus Lane:

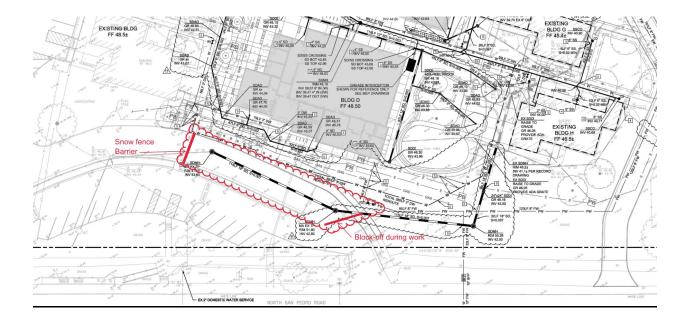

Construction is moving along at an excitingly swift pace! Please note, on Friday 11/16/18, in front of the school, construction will be excavating a new trench at the bus lane in order to install a new storm drain line. This work will move excess rain water out of the parking lot during heavy rainfall. A temporary barrier will be put in place to cordon off work from the construction. In order to minimize disruption to school drop-off and pick-up operations, steel plates will be used to cover trenches during non-work hours. The details of this work include saw cutting and demolition of existing asphalt, excavating a trench, installing new storm drain pipe, backfilling, compacting and repaving. See Quick Look schedule on next page.

Quick Look schedule below:

• Fri. 11/16: After buses arrive work hours begin just after 8:00 AM. Clean-up and trench plate will be back in place by 2:00 PM before school pickup

- Mon. 11/19 & Tues. 11/20: After buses arrive work hours begin just after 8:00 AM. Clean-up and trench plate will be back in place by 2:00 PM before school pickup
- Mon. 11/26 & Tues. 11/27: After buses arrive work hours begin just after 8:00 AM. Clean-up and trench plate will be back in place by 2:00 PM before school pickup
- **Wed. 11/28**: After buses arrive work hours begin just after 8:00 AM. Clean-up and trench plate will be back in place by 12:30 PM before school pickup

Projected Dates of Work: 11/16/18 to 11/28/18
