




Site Plan: Schematic Design



San Rafael High School
 Aquatics Center & Gym Modernization

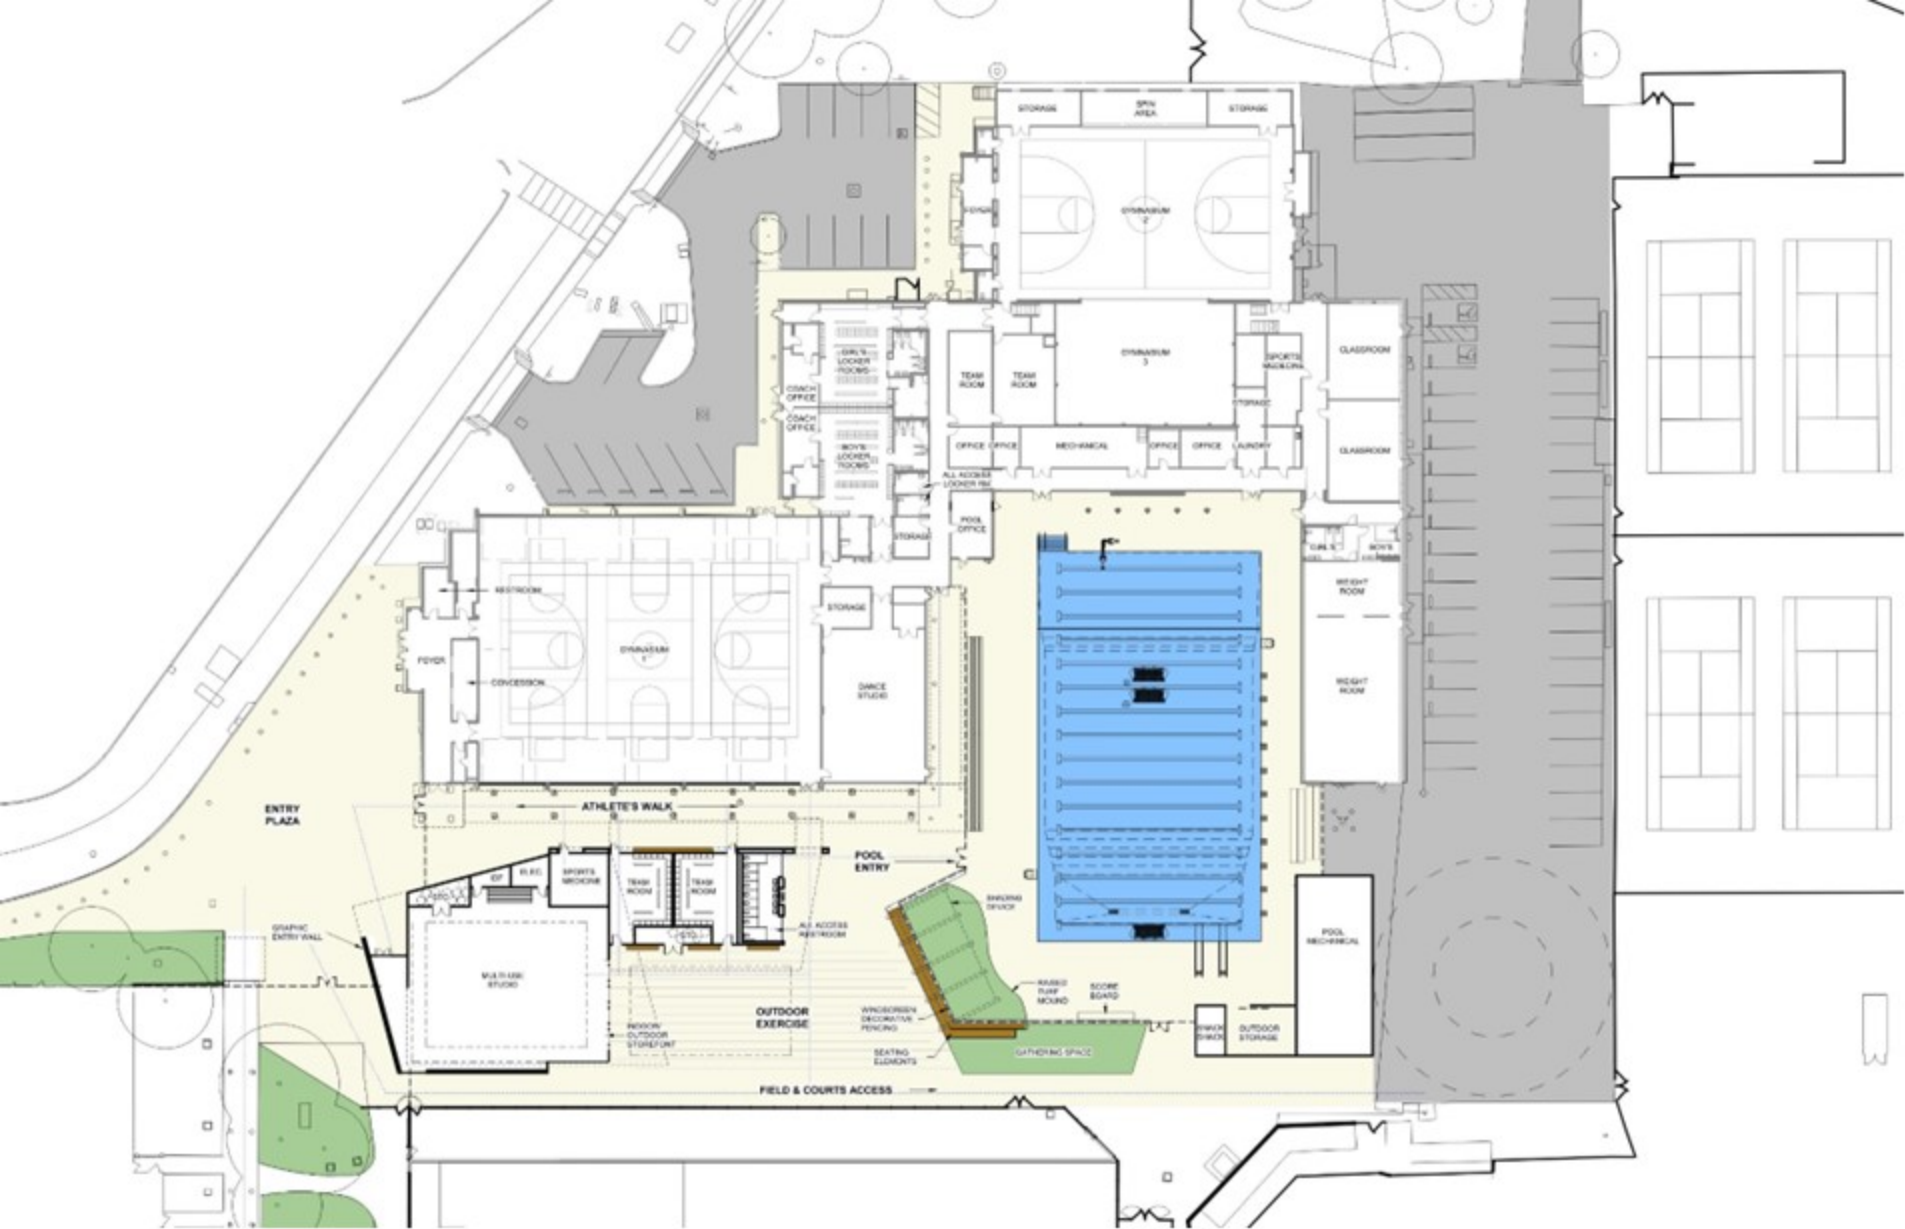

Aerial View: Schematic Design



**San Rafael High School
Aquatics Center & Gym Modernization**



Aerial View: Schematic Design



**San Rafael High School
Aquatics Center & Gym Modernization**

HIBSER YAMAUCHI
ARCHITECTS, INC. **HY**



Muti-Use Studio View: Schematic Design



**San Rafael High School
Aquatics Center & Gym Modernization**

HIBSER YAMAUCHI
ARCHITECTS, INC. **HY**



View from Mission Avenue: Schematic Design



**San Rafael High School
Aquatics Center & Gym Modernization**

HIBSER YAMAUCHI
ARCHITECTS, INC. **HY**




Aquatic Center & Gymnasium Modernization: Schematic Design



**San Rafael High School
Aquatics Center & Gym Modernization**

HIBSER YAMAUCHI
ARCHITECTS, INC. **HY**

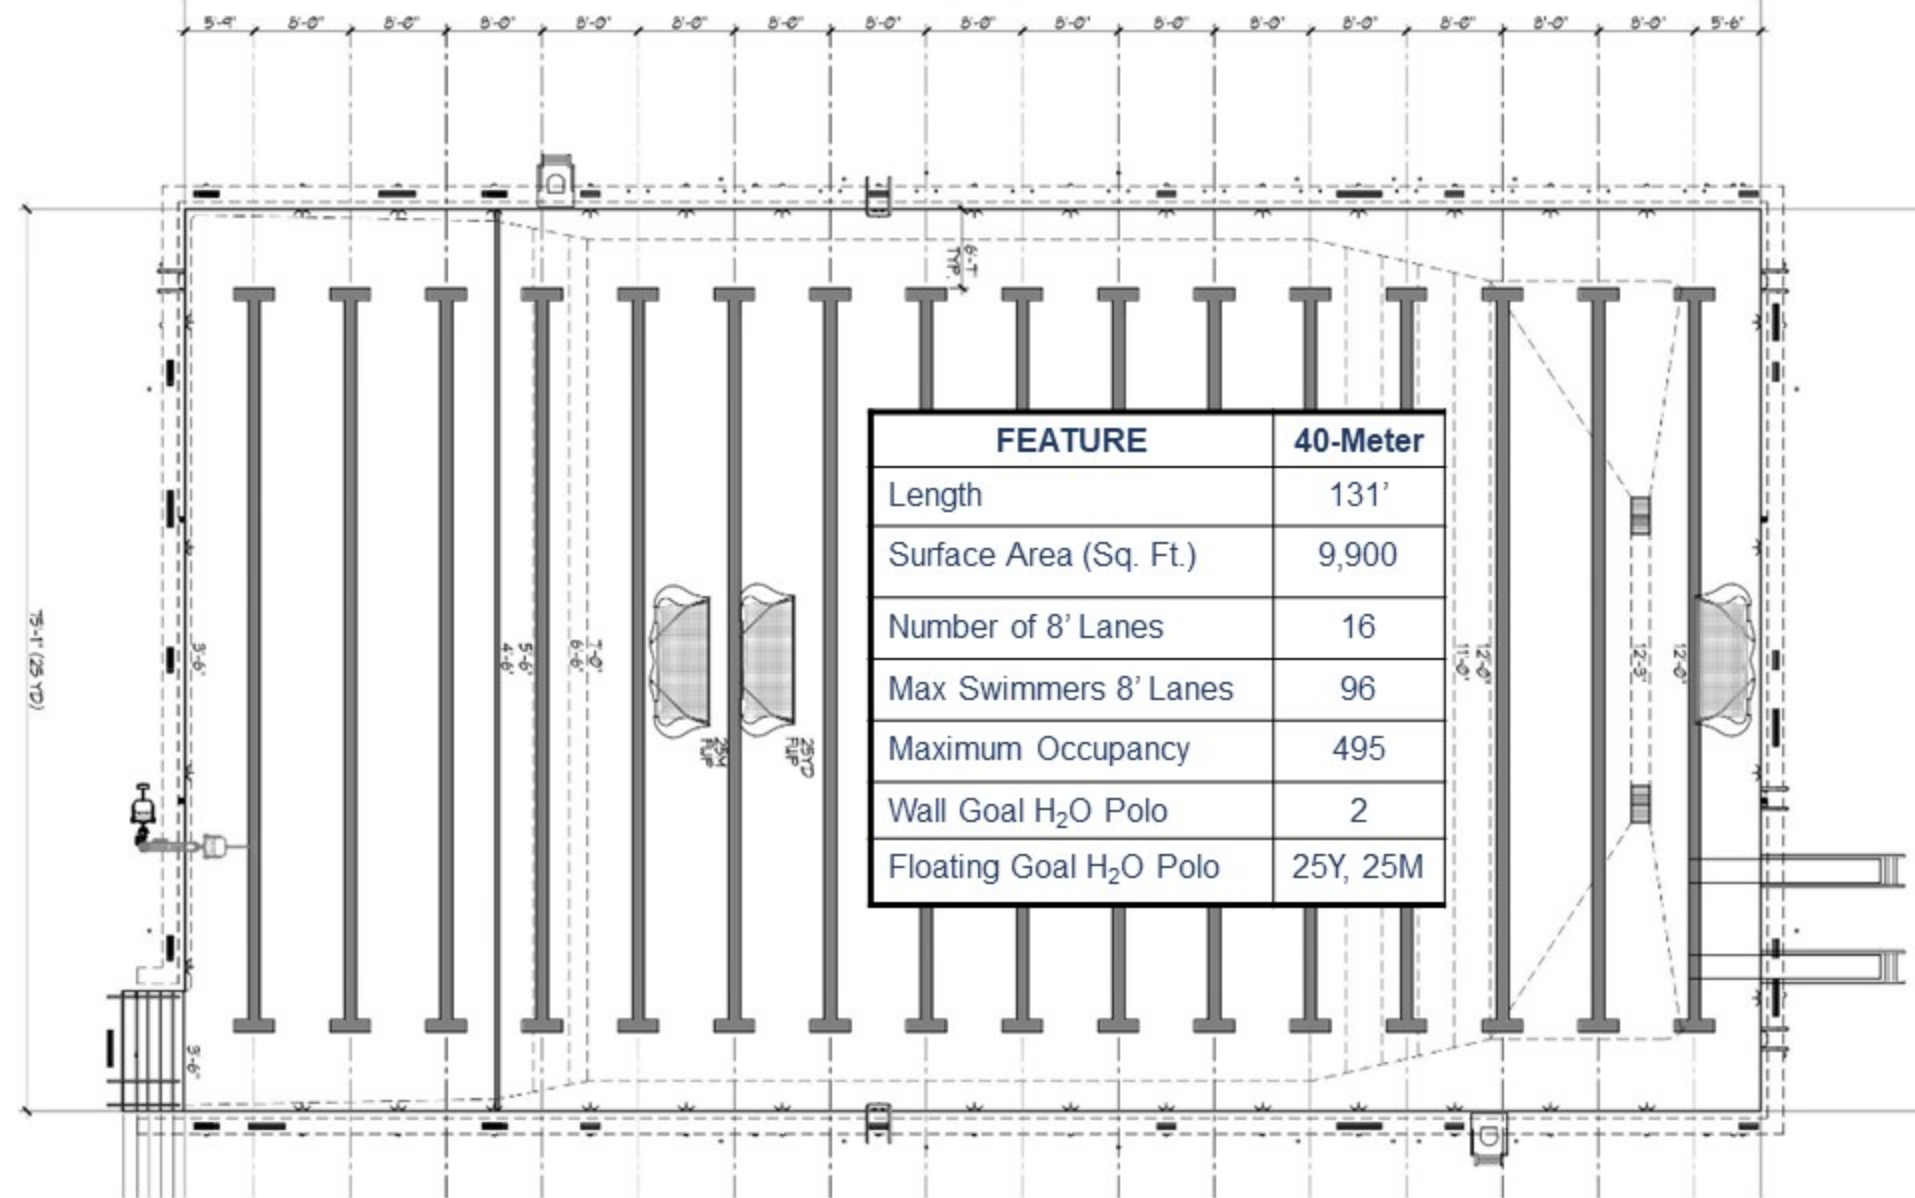


Swimming Pool Plan: Schematic Design



Front Entry

MATERIALS



INSPIRATION PHOTOS



MAIN ENTRY FROM INTERIOR



THIRD STREET ENTRY PLAN



MAIN ENTRY ELEVATION



Construction Phasing*

June 2024 – December 2025

***construction phasing in flux and subject to change**




San Rafael High School
Aquatics Center & Gym Modernization

HIBSER YAMAUCHI
ARCHITECTS, INC. **HY**

PHASE 1 (PORTABLES RELOCATION):
MAY - JUNE 2024 (SPRING)

• PAD PREP & UTILITIES

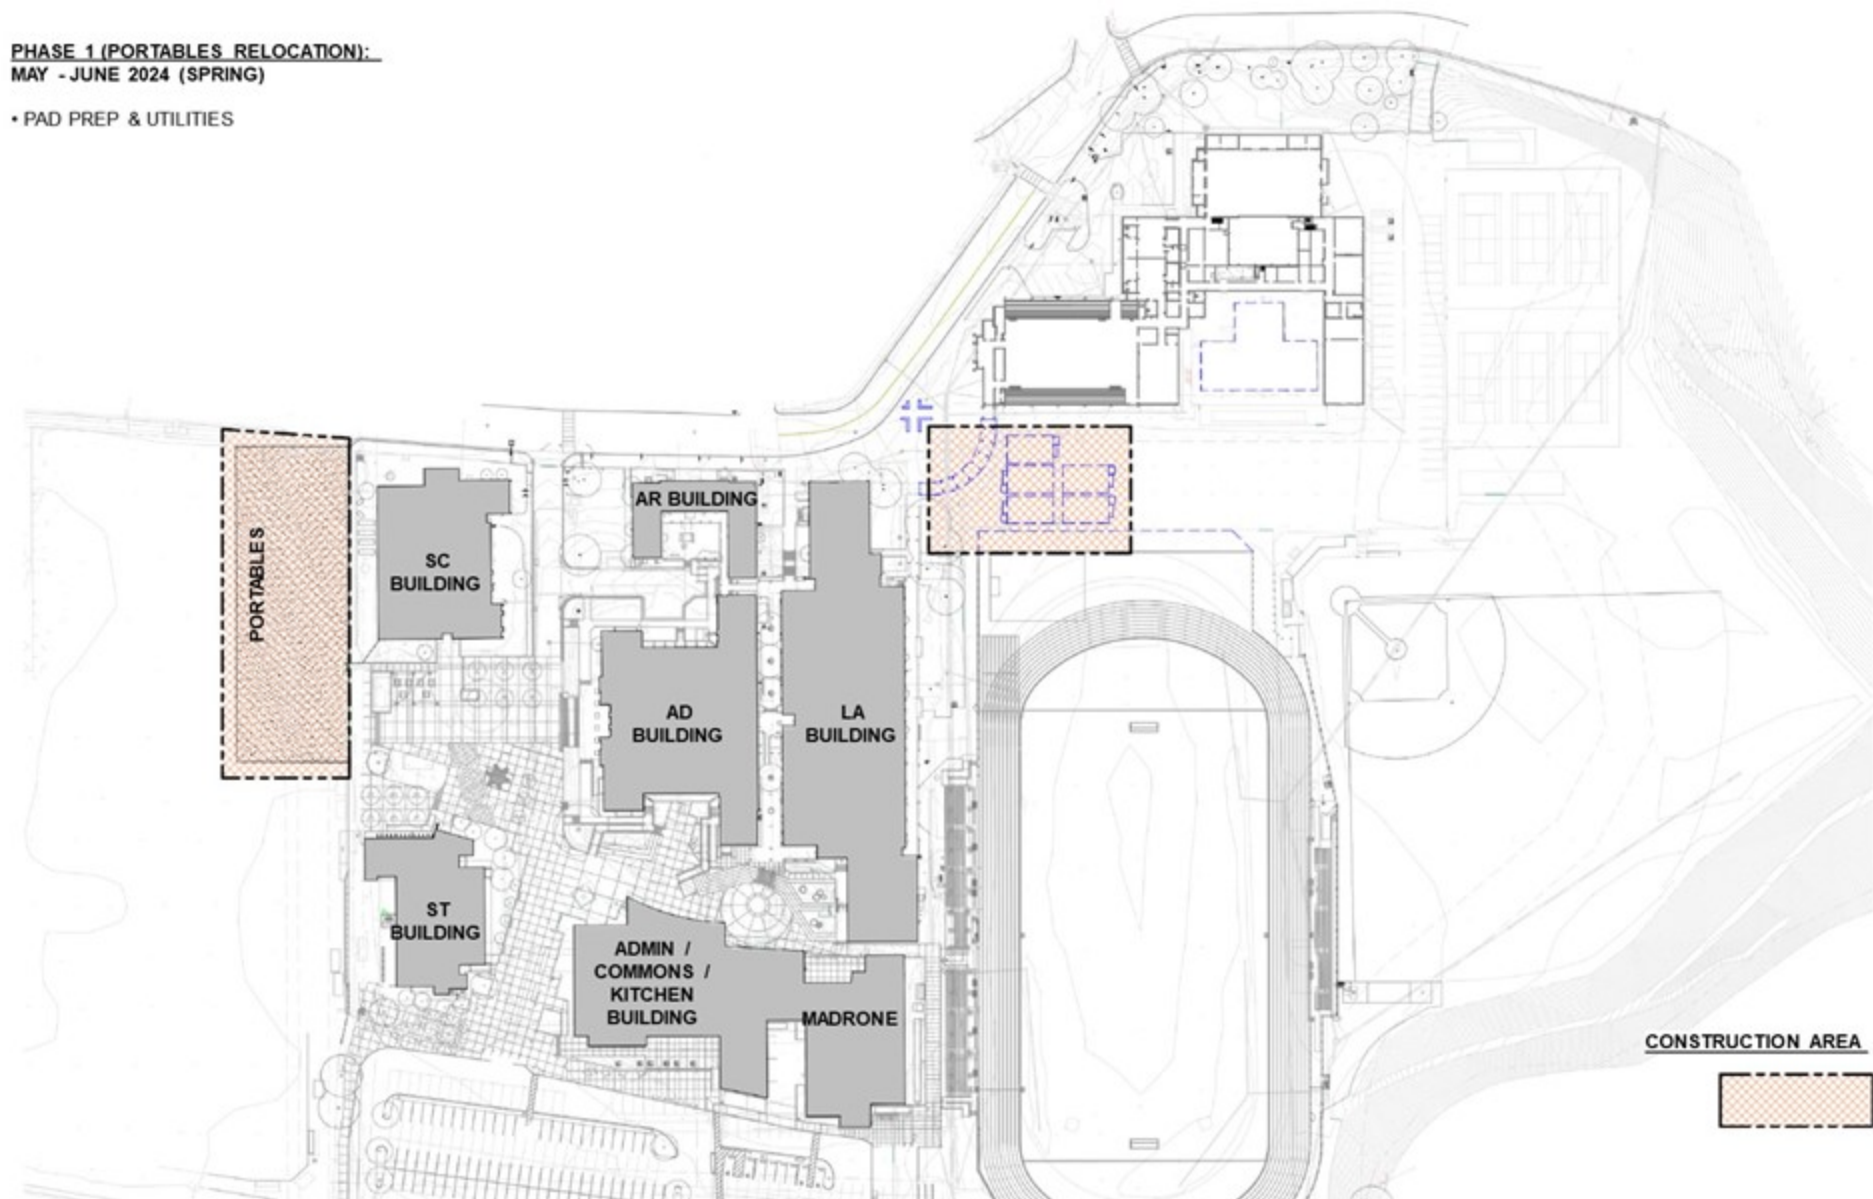

***construction phasing in flux and subject to change**



San Rafael High School
Aquatics Center & Gym Modernization

HIBSER YAMAUCHI
ARCHITECTS, INC. **HY**

PHASE 2 (AQUATIC CENTER INC. 1- SITE DEMOLITION/UTILITIES):
JUNE - AUGUST 2024 (SUMMER)


- SITE DEMOLITION
- SITE UTILITIES
- PG&E PAD PREPARATION

CONCURRENT PROJECTS:

- SOLAR PROJECTS BY OTHERS (JUNE - AUGUST 2024) TBD
- CAMPUS WIDE FIRE ALARM PROJECT (JUNE - NOVEMBER 2024)
- CAMPUS FENCING (JUNE - AUGUST 2024)
- TEMPORARY HOUSING- PORTABLES RELOCATION, CONNECTION, & FIT OUT
- COMMONS A/V

SCHOOL USE AREAS:
MAY - AUGUST 2024 (SUMMER)

- MACK BUILDING
- STEAM BUILDING

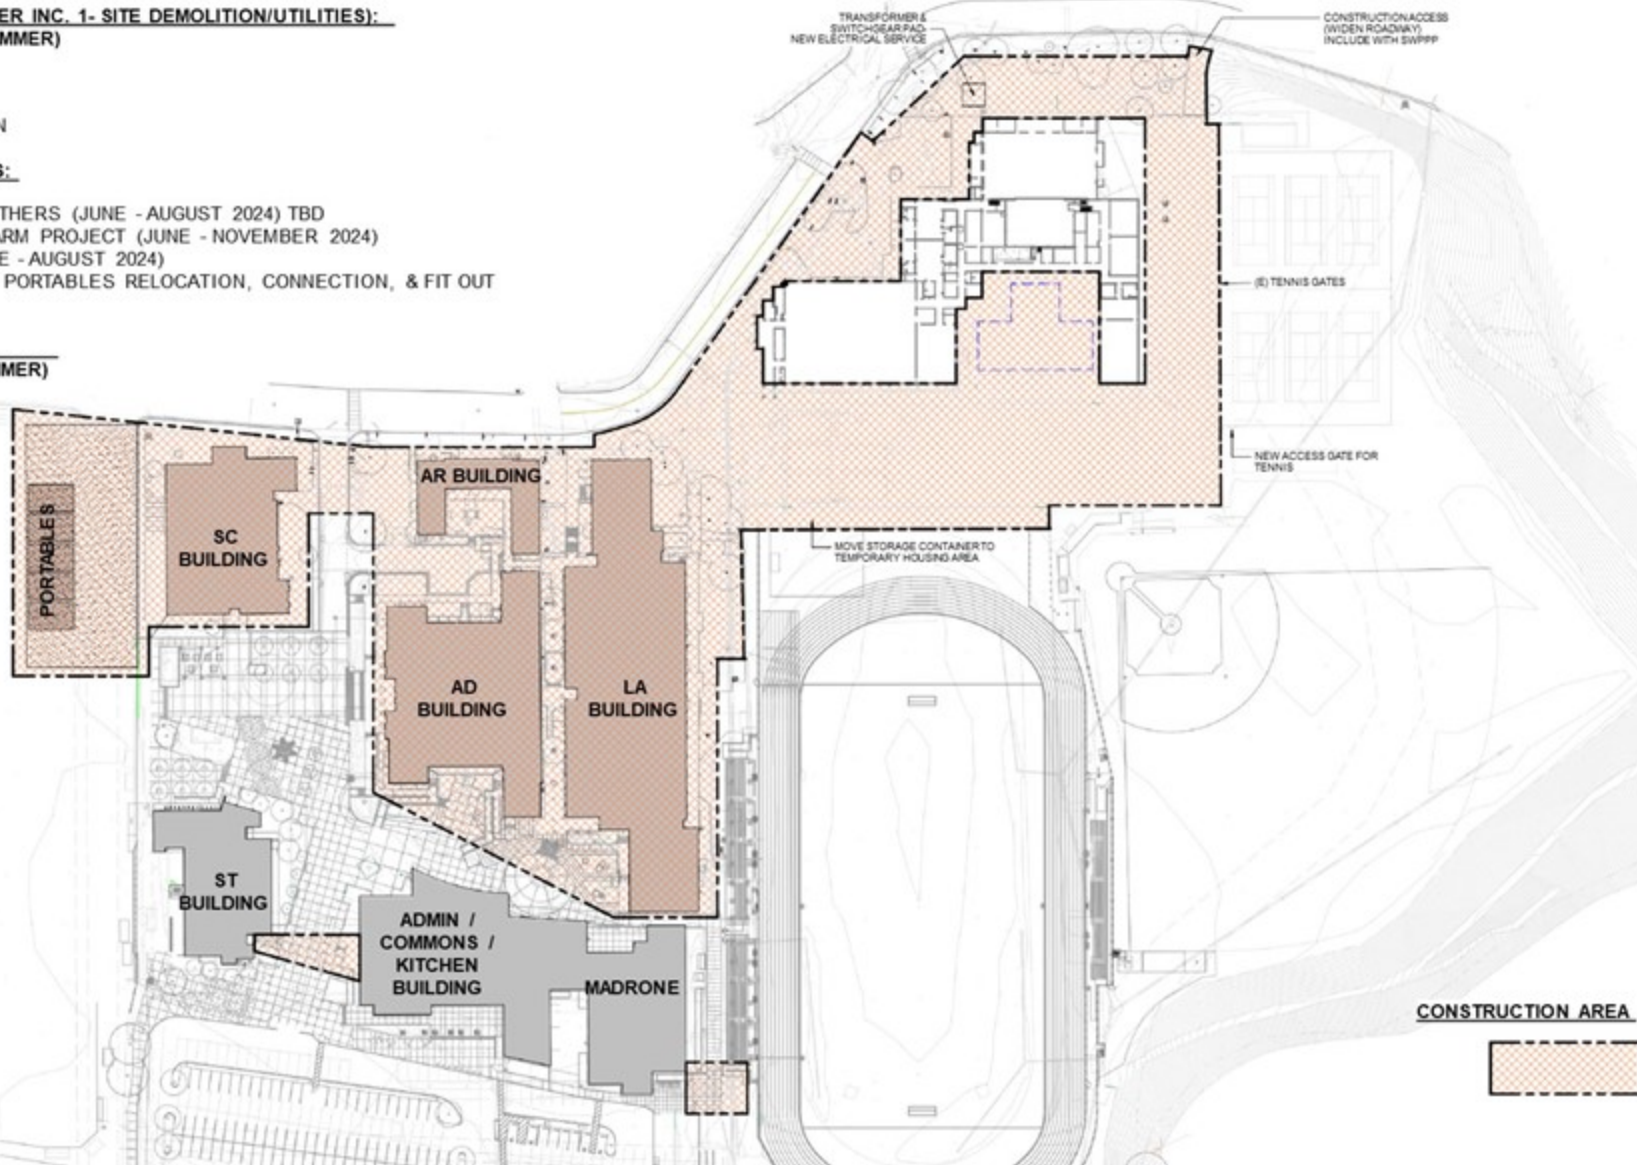

*construction phasing in flux and subject to change



PHASE 3 (AQUATIC CENTER & GYM MODERNIZATION) :
AUGUST 2024- JANUARY 2025 (FALL/WINTER)


- UTILITIES, PAVING, LANDSCAPE, COURTYARD- MISSION AVE
- PG&E PAD/EQUIPMENT PREP
- POOL
- PUMP HOUSE
- DAWG HOUSE
- GYM MODERNIZATION PHASE 1 SCOPE INCLUDES ALL AREAS OF THE GYM BUILDING EXCEPT GYM 2- AND CONNECTED AREAS (TEAM ROOMS, RESTROOMS, LOBBY)

SCHOOL USE IMPACT:
AUGUST 2024- JANUARY 2025 (FALL/WINTER)

- GYM 2 OPEN FOR PRACTICE USE ONLY
- P.E. RELOCATED TO TEMPORARY HOUSING @ SOCCER FIELD
- MISSION STREET PARKING LOTS CLOSED FOR CONTRACTOR ACCESS

CONCURRENT PROJECTS:

- FIRE ALARM PROJECT
(JUNE - NOVEMBER 2024)
- SOLAR PROJECT, BY OTHERS -TBC

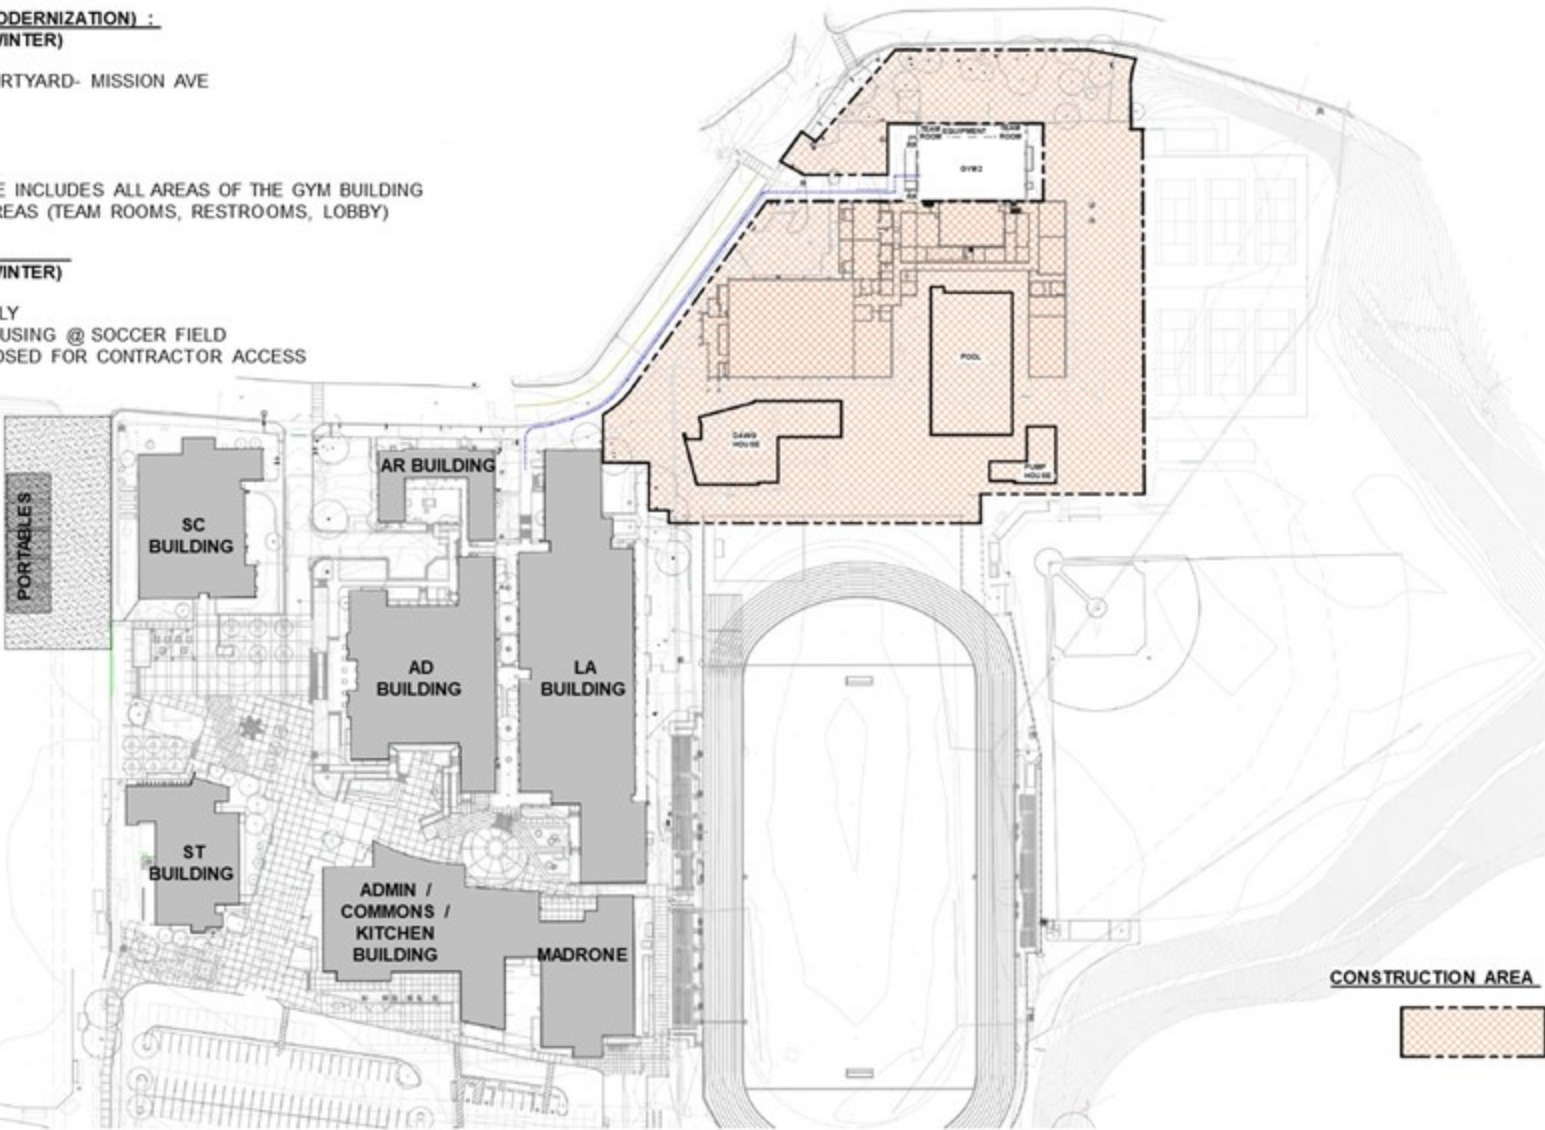

***construction phasing in flux and subject to change**




PHASE 4 (NEW CONSTRUCTION & GYM MODERNIZATION 2ND PART):
JANUARY 2025 - AUGUST 2025

- POOL
- PUMP HOUSE
- DAWG HOUSE
- GYM MODERNIZATION ALL AREAS EXCEPT GYM 1, LOBBY, & RESTROOMS.

SCHOOL USE IMPACT:
JANUARY 2025 - AUGUST 2025

- GYM 1 OPEN FOR LIMITED USE (PRACTICE ONLY)
- P.E. RELOCATED TO TEMPORARY HOUSING @ SOCCER FIELD
- MISSION STREET PARKING LOTS CLOSED FOR CONTRACTOR ACCESS

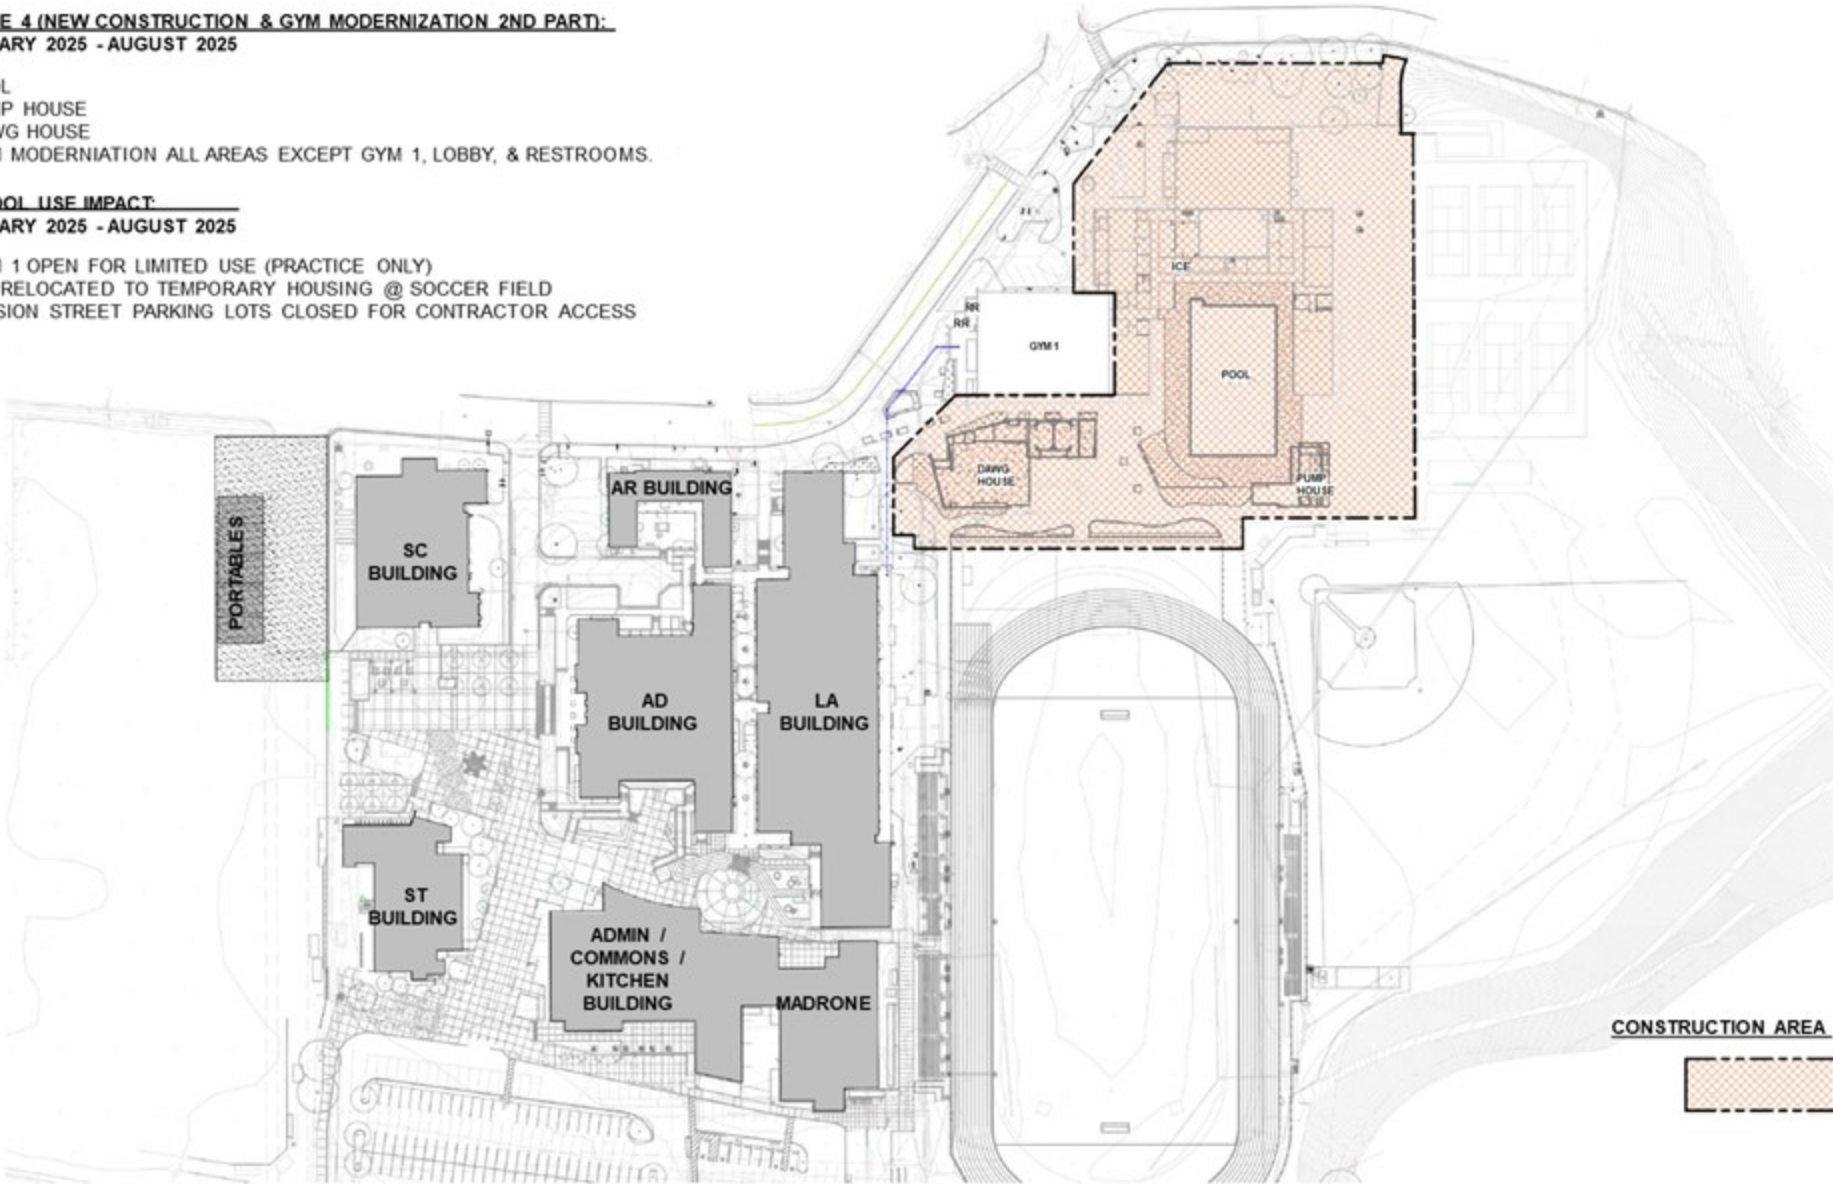


***construction phasing in flux and subject to change**



PHASE 5 (NEW CONSTRUCTION):
AUGUST 2025 - NOVEMBER 2025

- POOL
- PUMP HOUSE
- DAWG HOUSE
- REMAINING SITE WORK

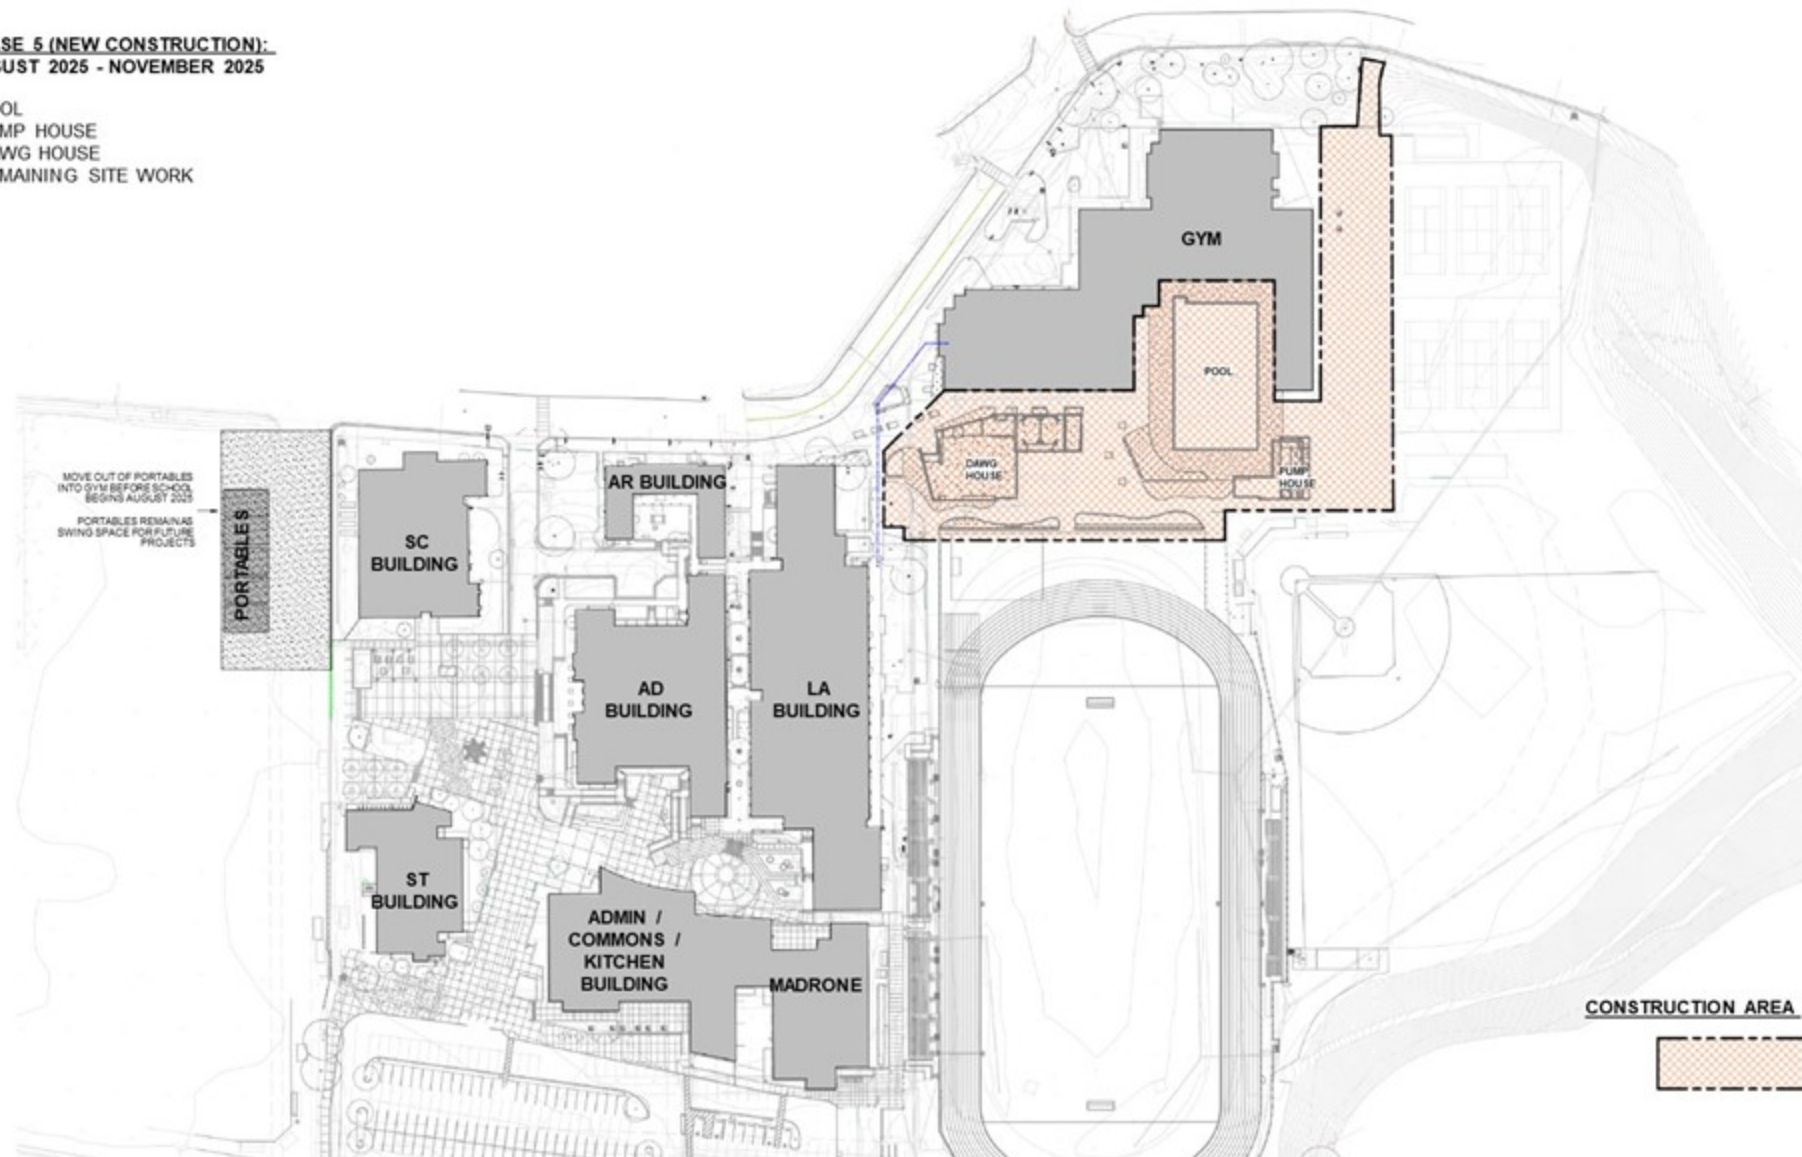

*construction phasing in flux and subject to change

